


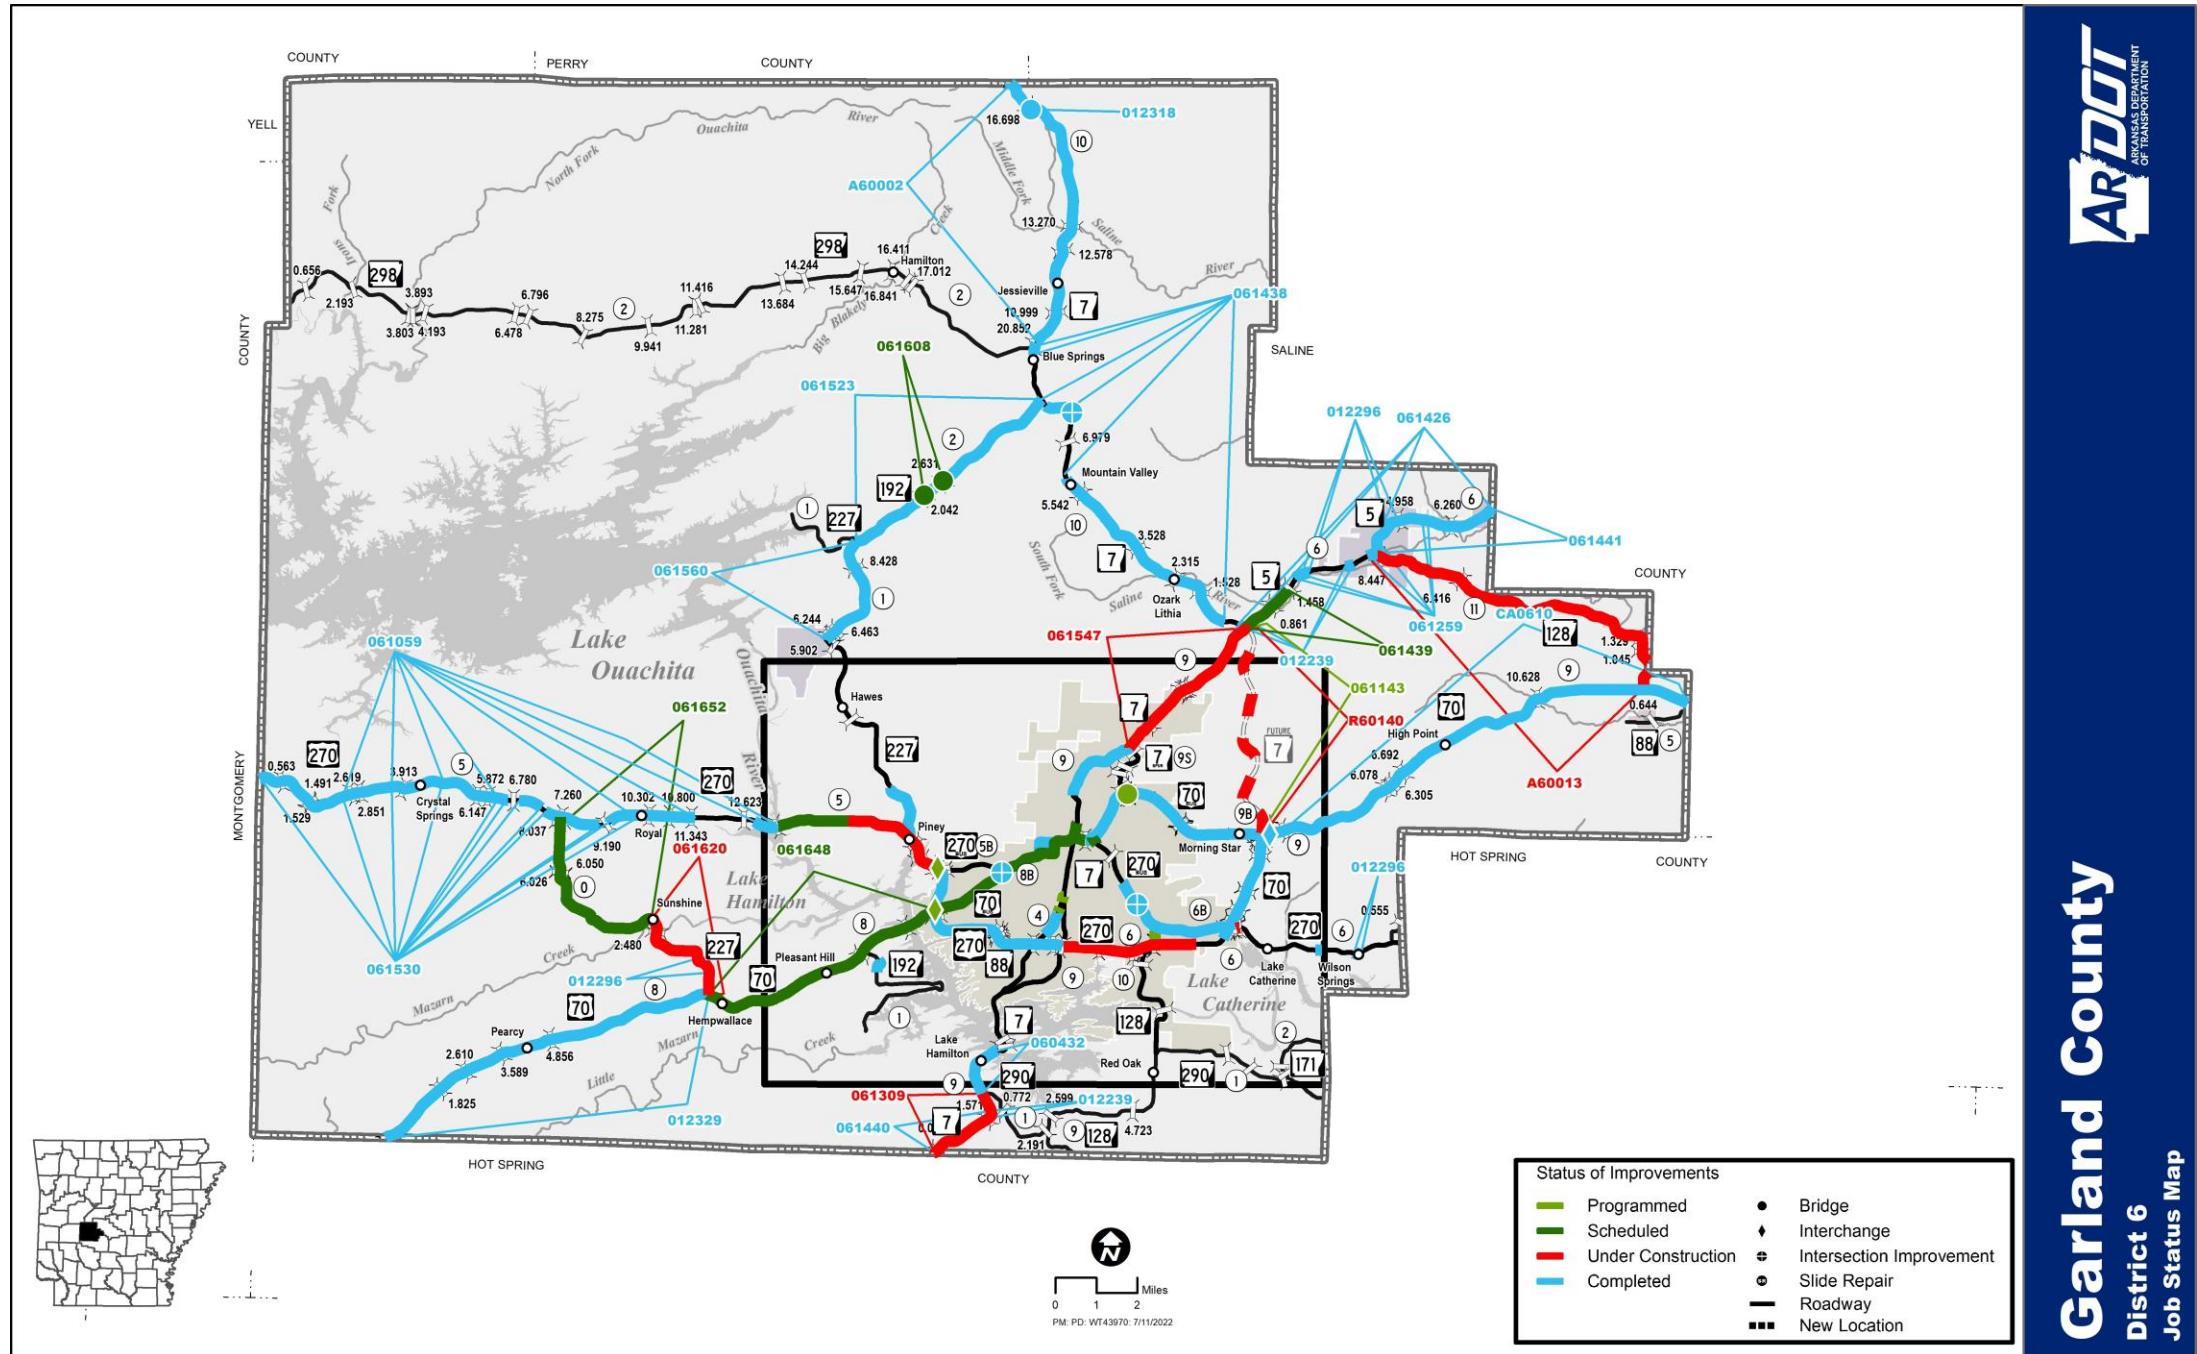

SUMMARY OF CONSTRUCTION PROJECTS

GARLAND COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
012288*	Low-Cost Safety Impvts. (Dists. 5, 6, 8 & 9) (S) Addt'l Rte.-Sec.: Various	5	6	Safety Improvements	Completed	Oct. 2017	Jun. 2018	3.81	\$253,442	43.27	\$2,878,336
012296	Districts 2, 6, 7 & 8 Pavement Friction Impvts. (Sel. Secs.) (S) Addt'l Rte.-Sec.: Various	5	6	Safety Improvements	Completed	Jan. 2018	Oct. 2018	1.96	\$861,257	6.10	\$2,648,885
012318	Middle Fork Saline River & Dry Run Creek Strs. & Apprs. (S) Addt'l Rte.-Sec.: Perry 7-11	7	10	Structure & Approaches	Sub. Completed	Jan. 2020	Jun. 2022	0.19	\$1,919,337	0.45	\$4,545,799
012329	Glenwood – Hwy. 227 (S) Addt'l Rte.-Sec.: Hot Spring 70-7; Montgomery 70-6; Pike 70-5	70	8	Resurfacing	Completed	May. 2019	Jun. 2020	8.07	\$2,675,850	18.14	\$6,032,225
012335*	Foot Trail Shelter Modifications (RTP-18) (S)			Enhancement	Completed	Oct. 2019	Mar. 2021	-	\$5,250	-	\$26,250
012350*	Districts 2, 3, 6 & 7 Bridge Preservation (2020) (S) Addt'l Rte.-Sec.: Various	270	6	Bridge Rehabilitation	Completed	Apr. 2020	Mar. 2021	0.07	\$112,112	1.81	\$2,898,898
012361*	Statewide UTBWC Impvts. (2020) (S) Addt'l Rte.-Sec.: Various			Safety Improvements	Under Construction	Nov. 2020	Late 2022	0.62	\$179,137	31.98	\$9,240,000
012387*	Statewide Underwater Br. Inspection (Phase XIII) (S) Addt'l Rte.-Sec.: Various	7	9	Miscellaneous	Programmed			-	-	-	-
012406*	Districts 1, 5, 6 & 10 Bridge Preservation (2022) (S) Addt'l Rte.-Sec.: Various			Bridge Rehabilitation	Under Construction	May. 2022	Mid 2023	-	\$963,505	-	\$7,187,312
060153*	Belding St. Split Out & Shady Grove Rd.Intersection	CS		Safety Improvements	Programmed			-	< \$1 M	-	< \$1 M
060250*	Cutter Morning Star School Dist. Sidewalks (TAP-21) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
060432	Hwy. 290 – Ouachita River Bridge (S)	7	9	Major Widening	Completed	Apr. 2017	Jan. 2019	1.41	\$10,698,642	1.41	\$10,698,642
061059	Hot Springs – West (Passing Lanes) (S)	270	5	Passing Lanes	Completed	Nov. 2010	Aug. 2013	4.46	\$11,272,060	4.46	\$11,272,060
061101*	Hwy. 270B – Ouachita River (Hot Springs) P.E.	128	10	PE Only	Programmed			-	-	-	-
061113	Hwy. 270 – Printers Place (Higdon Ferry Rd.) (Hot Springs) (S)	88	4	Major Widening	Completed	May. 2012	Jun. 2013	0.47	\$4,697,041	0.47	\$4,697,041
061143	Hwy. 70 East – Hwy. 7 North (Add'l. Lanes) (S)	New		Major Widening	Programmed			5.49	\$50 - \$75 M	5.49	\$50 - \$75 M
061203	North of Hwy. 270 – Hwy. 270B (Hot Springs) (S)	128	10	Major Widening	Programmed			0.40	\$1 - \$3 M	0.40	\$1 - \$3 M
061214	Printers Place – Crawford St. (Higdon Ferry Rd.) (Hot Springs) (S)	88	4	Major Widening	Completed	Sep. 2014	Jan. 2016	0.19	\$3,901,687	0.19	\$3,901,687
061238*	Stokes Creek Drainage Repair (Hwy. 270) (Hot Springs) (S)	270	5	Miscellaneous	Programmed			-	-	-	-
061242*	Valley Street Creekwalk (Phase II) (S)	New		Enhancement	Completed	Oct. 2009	Jul. 2014	-	\$115,359	-	\$115,359
061254	Garland Co. Area Hdq./R.E. Office (S)	New		Buildings	Completed	Feb. 2012	Aug. 2013	-	\$946,477	-	\$946,477
061259	Hwy. 7 – Hot Springs Village (Safety Impvts.) (S)	5	6	Safety Improvements	Completed	Feb. 2012	Jul. 2013	0.89	\$3,490,333	0.89	\$3,490,333
061285	Hwy. 70 East Intchnng. (Hot Springs) (Ph. III) (S)	270	6	Interchange Improvements	Completed	Apr. 2011	Mar. 2013	-	\$7,488,684	-	\$7,488,684

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

GARLAND COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
061309	Mitzi Pkwy. – Hwy. 290 (Safety Impvts.) (Sel. Secs.) (S)	7	9	Major Widening Structure & Approaches	Under Construction	Aug. 2020	<i>Late 2023</i>	2.31	\$7,007,888	3.80	\$11,528,128
	Addt'l Rte.-Sec.: Hot Spring 7-8										
061312*	Hot Springs Creek Str. & Apprs. (Hot Springs) (S)	CS		Structure & Approaches	Completed	Nov. 2014	Oct. 2015	-	\$740,367	-	\$740,367
061314	Crawford St. – Hwy. 7 North (Hot Springs) (S)	88	4	New Location	Programmed			0.14	\$1 - \$3 M	0.14	\$1 - \$3 M
061319*	Hot Springs Creek Greenway Trail (Phase III) (ATEP-11) (S)			Enhancement	Completed	Oct. 2012	Jul. 2014	-	\$189,976	-	\$189,976
061329*	Whittington Ave. – Hwy. 5 P.E.	7	9	PE Only	Completed		Mar. 2018	6.17	\$326,005	6.17	\$326,005
061340*	Valley Street Creekwalk (Ph. III) (Hot Springs) (S)			Enhancement	Completed	Apr. 2012	Dec. 2014	-	\$50,286	-	\$50,286
061343	I-40 & Hwy. 270 Overhead Sign Structures Replacement (S)			Safety Improvements	Completed	Jun. 2012	Dec. 2012	-	\$119,211	-	\$212,877
061368	Hwy. 270B – Hwy. 70 (Hot Springs) (Overlay) (S)	270	5	Resurfacing	Completed	Mar. 2012	Sep. 2012	1.06	\$622,036	1.06	\$622,036
061374	Hwy. 270B – East (Hot Springs) (Overlay) (S)	70	8B	Resurfacing	Completed	May. 2012	Nov. 2012	1.57	\$584,272	1.57	\$584,272
061391*	Stokes Creek Str. & Apprs. (Hot Springs) (S)	CS		Structure & Approaches	Completed	Jan. 2016	Aug. 2016	0.03	\$438,012	0.03	\$438,012
061397*	Lake Ouachita Vista Trail Segment 8 (S)			Enhancement	Completed	Nov. 2013	May. 2014	-	\$101,080	-	\$101,080
061398*	Blue Heron Trail (Hot Springs) (S)			Enhancement	Completed	Sep. 2014	Jul. 2015	-	\$115,864	-	\$115,864
061426	Hwy. 7 – Saline Co. Line (Sel. Secs.) (Overlay) (S)	5	6	Resurfacing	Completed	Feb. 2014	Jun. 2014	3.19	\$559,588	3.19	\$559,588
	Addt'l Rte.-Sec.: Garland 7-10										
061429	Malvern Ave. – East (Hot Springs) (Overlay) (S)	70	9B	Resurfacing	Completed	Apr. 2014	Sep. 2014	1.30	\$524,200	1.30	\$524,200
061431	Hwy. 7S – Hwy. 70 Intchn. (Cable Median Barrier) (S)	70	9	Safety Improvements	Completed	Sep. 2014	Jun. 2015	4.30	\$1,206,660	4.30	\$1,206,660
	Addt'l Rte.-Sec.: Garland 70-9B										
061438	Bryant Rd. – Hwy. 298 West (Safety Impvts.) (Sel. Secs.) (S)	7	10	Safety Improvements	Sub. Completed	Jan. 2020	Jan. 2022	3.46	\$6,739,186	3.46	\$6,739,186
061439	Hwy. 7 – Deerpark Rd. (Safety Impvts.) (S)	5	6	Safety Improvements	Scheduled	Jan. 2023		1.28	\$5 - \$10 M	1.28	\$5 - \$10 M
061440	Sycamore Dr. – Hwy. 290 (Safety Impvts.) (S)	7	9	Safety Improvements	Completed	Sep. 2015	Nov. 2015	1.74	\$174,239	13.80	\$1,381,897
	Addt'l Rte.-Sec.: Hot Spring 7-8										
061441	Hwy. 128 – Benton (Safety Impvts.) (S)	5	6	Safety Improvements	Completed	Feb. 2016	Sep. 2017	3.18	\$1,199,724	20.93	\$7,896,298
	Addt'l Rte.-Sec.: Saline 5-7										
061449*	Hot Springs Trail Enhancements (S)	New		Enhancement	Completed	Sep. 2015	Jun. 2016	-	\$97,500	-	\$97,500
061455*	Hot Springs Ped. Impvts. (FLAP) (S)	CS		Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061471	Hwy. 70B/West St. Louis Signal (Hot Springs) (S)	70	8B	Safety Improvements	Completed	Apr. 2018	Mar. 2019	-	\$252,027	-	\$252,027
	Addt'l Rte.-Sec.: Garland CS										
061479*	Hot Springs Schools Ped. Connectors (SRTS-15) (S)			Enhancement	Under Construction	Jul. 2020		0.28	\$93,586	0.28	\$93,586
061483*	Hollywood Ave. Multi-Use Trail (Hot Springs) (TAP-15) (S)			Enhancement	Completed	Aug. 2020	Mar. 2022	0.44	\$205,750	0.44	\$205,750

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

GARLAND COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
061484*	Hot Springs Creek Greenway Trail (Ph. 5) (TAP-15) (S)			Enhancement	Under Construction	Nov. 2016		-	\$749,500	-	\$749,500
061514	Hwy. 270 – North (S)	227	1	Resurfacing	Completed	Apr. 2018	Sep. 2018	1.31	\$452,114	1.31	\$452,114
061519	Spring St. – Persimmon St. (Hot Springs) (S)	70	9B	Resurfacing	Completed	May. 2018	Sep. 2018	3.11	\$1,559,992	3.11	\$1,559,992
061520	Hwy. 70 – Hwy. 7 (Hot Springs) (S)	270	5	Resurfacing	Completed	Apr. 2019	Oct. 2019	3.66	\$4,523,979	3.66	\$4,523,979
061523	Hwy. 227 – Hwy. 7 (S)	192	2	Resurfacing	Completed	May. 2018	Nov. 2018	5.91	\$1,371,757	5.91	\$1,371,757
061530	Montgomery Co. Line – Royal (Sel. Secs.) (S)	270	5	Resurfacing	Completed	Feb. 2018	Jun. 2018	6.77	\$1,537,248	6.77	\$1,537,248
061534*	Hot Springs SRTS (TAP-16) (S)			Enhancement	Under Construction	Aug. 2020		0.21	\$106,357	0.21	\$106,357
061535*	Hot Springs Creek Greenway Trail Ph. 6 (TAP-16) (S)			Enhancement	Under Construction	May. 2022		-	\$668,679	-	\$668,679
061536*	Hot Springs National Park Trail Impvts. (TAP-16) (S)			Enhancement	Completed	Feb. 2017	Jun. 2021	-	\$290,422	-	\$290,422
061546	Whittington Ave. – Hwy. 7S (Hot Springs) (S)	7	9	Resurfacing	Completed	Feb. 2018	Oct. 2018	2.00	\$705,322	2.00	\$705,322
061547	Hwy. 7S – Hwy. 5 (S)	7	9	Major Widening Resurfacing	Under Construction	Sep. 2020	Late 2023	4.29	\$18,051,958	4.29	\$18,051,958
061555*	Hwy. 270 & Hwy. 7 Impvts. (Hot Springs) (S) Addt'l Rte.-Sec.: Garland 270-5	7	9	Study	Completed	Nov. 2017	Jan. 2022	-	\$500,000	-	\$500,000
061560	Mountain Pine – Hwy. 192 (Safety Impvts.) (S)	227	1	Safety Improvements	Completed	Feb. 2018	May. 2018	3.05	\$342,284	3.05	\$342,284
061562*	Southwest Trail Design Addt'l Rte.-Sec.: Pulaski New; Saline New	New		Enhancement	Programmed			-	< \$1 M	-	\$1 - \$3 M
061574	Hwy. 270B/Lakeside Rd. Signal (Hot Springs) (S)	270	6	Safety Improvements	Sub. Completed	Nov. 2019	Oct. 2020	-	\$231,254	-	\$231,254
061577*	Hot Springs Wayfinding (S)			Enhancement	Under Construction	Jan. 2022		-	\$407,852	-	\$407,852
061586	Hwy. 270 – Cedar Creek (S)	70	9	Resurfacing	Completed	Jun. 2020	Nov. 2020	2.89	\$2,470,030	2.89	\$2,470,030
061601*	Hot Springs Creek Greenway Trail Ph. 6B (TAP-18) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061608	Hwy. 192 Strs. & Apprs. (Garland Co.) (S)	192	2	Structure & Approaches	Scheduled	Jun. 2023		0.43	\$1 - \$3 M	0.43	\$1 - \$3 M
061620	Hwy. 70 – Oakgrove Rd. (Safety Impvts.) (S)	New		Safety Improvements	Under Construction	Aug. 2020	Late 2023	2.82	\$1,599,690	2.82	\$1,599,690
061627	Hwy. 7 Spur North & South (Widening) (Hot Springs) (S)	7	9	Major Widening	Programmed			1.68	-	1.68	-
061635*	Hot Springs Emory & Seventh St. Sidewalks (TAP-19) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061643*	District 6 Sealing Program (2020) (S) Addt'l Rte.-Sec.: Various	227	0	Sealing	Programmed			17.63	< \$1 M	69.72	\$1 - \$3 M
061645	Albert Pike & Airport Rd. Intchnng. Impvts. (Hot Springs) (S)	270	5	Safety Improvements	Programmed			-	\$20 - \$30 M	-	\$20 - \$30 M
061648	Hwy. 227 – Hwy. 270 (S)	70	8	Resurfacing	Scheduled	May. 2023		6.29	\$3 - \$5 M	6.29	\$3 - \$5 M
061649	Hwys. 7, 70B, & 270B (Sel. Secs.) (Hot Springs) (S) Addt'l Rte.-Sec.: Garland 70-8B/9B, 270-6B	7	9	Resurfacing	Scheduled	Feb. 2023		5.02	\$3 - \$5 M	5.02	\$3 - \$5 M

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

GARLAND COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
061652	Sunshine – Hwy. 270 (S)	227	0	Resurfacing	Scheduled	2024		4.53	< \$1 M	4.53	< \$1 M
061709*	Overhead Sign Strs. & Signs Replacement (Central AR) (S) Addt'l Rte.-Sec.: Garland 270-5/6; Pulaski 30-23, 440-2; Saline 30-22	70	9	Safety Improvements	Under Construction	May. 2021	Mid 2023	-	\$1,050,191	-	\$1,680,308
061723*	Hot Springs Creek Greenway Trail Ph. 6C (TAP-20) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061737	Ouachita River – Fleetwood Dr. (Widening) (S)	270	5	Major Widening	Scheduled	Jun. 2024		1.67	\$20 - \$30 M	1.67	\$20 - \$30 M
061742	Gulpha Creek Strs. & Apprs. (Hot Springs) (S)	70	9	Structure & Approaches	Programmed			-	\$3 - \$5 M	-	\$3 - \$5 M
061748*	Mill Creek Str. & Apprs. (S)	600	21	Structure & Approaches	Scheduled	Mar. 2025		-	< \$1 M	-	< \$1 M
061755	Vineyard St. – Central Ave. (Hwy. 88) (Hot Springs) (S)	88	4	Minor Widening	Programmed			0.16	< \$1 M	0.16	< \$1 M
A60002	Hwy. 298 – Perry Co. Line (S)	7	10	Resurfacing	Sub. Completed	Jan. 2021	Sep. 2021	7.36	\$1,970,670	7.36	\$1,970,670
A60006	Hollywood Ave. – Hwy. 270 (Hot Springs) (S)	270	6B	Resurfacing	Sub. Completed	Apr. 2021	Oct. 2021	3.26	\$1,734,208	3.26	\$1,734,208
A60007*	District 6 Resurfacing Program (2021) (S) Addt'l Rte.-Sec.: Various	88	5	Resurfacing	Completed		Jun. 2022	4.40	\$96,936	49.36	\$1,159,267
A60013	Hwy. 70 – Hwy. 5 (S) Addt'l Rte.-Sec.: Saline 128-11	128	11	Resurfacing	Under Construction	Feb. 2022	Late 2022	8.08	\$4,097,758	8.38	\$4,249,903
A60014	Hwy. 7 – AKMD RR Overpass (Sel. Secs.) (S)	270	6	Resurfacing	Under Construction	May. 2022	Late 2022	3.22	\$4,034,880	3.22	\$4,034,880
A60020*	District 6 Resurfacing Program (2023) (S) Addt'l Rte.-Sec.: Various	171	4	Resurfacing	Programmed			10.45	< \$1 M	69.05	\$1 - \$3 M
BR2604*	Lockett Creek Str. & Apprs. (S)	CR		Structure & Approaches	Completed	Sep. 2014	Aug. 2015	-	\$1,027,356	-	\$1,027,356
BR2605*	Lost Cr. & S. Fork Little Mazarn Cr. Strs. &	CR		Structure & Approaches	Under Construction	Jan. 2022	Late 2024	0.66	\$4,353,662	0.66	\$4,353,662
C26001*	Hot Springs Golf Links Rd Overlay(sel Secs)(s)	CS		Resurfacing	Completed	Sep. 2013	May. 2014	1.61	\$331,631	1.61	\$331,631
C26002*	Hot Springs Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	May. 2018	Oct. 2018	1.85	\$325,817	1.85	\$325,817
C26003*	Mountain Pine Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Feb. 2018	Aug. 2018	5.37	\$379,387	5.37	\$379,387
C26004*	Fountain Lake Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	May. 2018	Oct. 2018	0.91	\$143,963	0.91	\$143,963
C26006*	Mountain Pine Overlay No. 2 (S)	CS		Resurfacing	Under Construction	Jun. 2022		1.37	\$399,836	1.37	\$399,836
C26007*	Fountain Lake Overlay (S)	CS		Resurfacing	Under Construction	Feb. 2022	Late 2022	2.48	\$381,719	2.48	\$381,719
C26008*	Hot Springs Lakeshore Dr. Overlay (S)	CS		Resurfacing	Under Construction	May. 2022	Late 2022	1.97	\$582,973	1.97	\$582,973
C76040*	Lonsdale & Rockport Overlay (Sel. Secs.) (S) Addt'l Rte.-Sec.: Hot Spring CS	CS		Resurfacing	Completed	Jul. 2017	Nov. 2017	1.63	\$171,223	3.88	\$407,574
CA0607	Fleetwood Dr. – Hwy. 227 (Widening) (S)	270	5	Major Widening	Under Construction	Apr. 2021	Late 2023	1.75	\$22,614,577	1.75	\$22,614,577
CA0610	Hot Springs – I-30 (Widening) (S) Addt'l Rte.-Sec.: Saline 70-10	70	9	Major Widening	Completed	Dec. 2016	May. 2018	11.02	\$49,213,461	17.58	\$78,528,337

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

GARLAND COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
CA0611*	Ouachita River – Hwy. 227 (Widening) P.E.	270	5	PE Only	Programmed			3.38	-	3.38	-
R60016*	East – West Arterial (Hot Springs) P.E.	New		PE Only	Programmed			5.16	-	5.16	-
R60140	Hwy. 70 East – Hwy. 7 North (F)	New		New Location	Under Construction	Nov. 2019	Late 2022	5.82	\$75,151,271	5.82	\$75,151,271
SA2666*	Garland Co. Overlay No. 12 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jul. 2013	Jan. 2014	4.40	\$839,295	4.40	\$839,295
SA2667*	Hwy. 227 - East (Overlay) (S)	CR		Resurfacing	Completed	Apr. 2015	Jul. 2015	7.32	\$696,021	7.32	\$696,021
SA2668*	Garland Co. Overlay No. 13 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jun. 2016	Oct. 2016	7.92	\$988,534	7.92	\$988,534
SA2669*	Garland Co. Widening & Overlay (Sel.secs.)(s)	CR		Resurfacing	Completed	May. 2017	Sep. 2017	6.21	\$1,019,883	6.21	\$1,019,883
SA2670*	Hwy. 7 - East (Overlay) (S)	CR		Resurfacing	Sub. Completed	Aug. 2020	Nov. 2020	5.07	\$775,474	5.07	\$775,474
SA2671*	Kelton St. - East (Overlay) (S)	CR		Resurfacing	Under Construction	Apr. 2022	Late 2022	1.93	\$1,145,335	1.93	\$1,145,335
Totals For All Projects In Garland County								202.02	\$322,722,129		

* Job not shown on county map.
