




Prairie County

District 6
Job Status Map

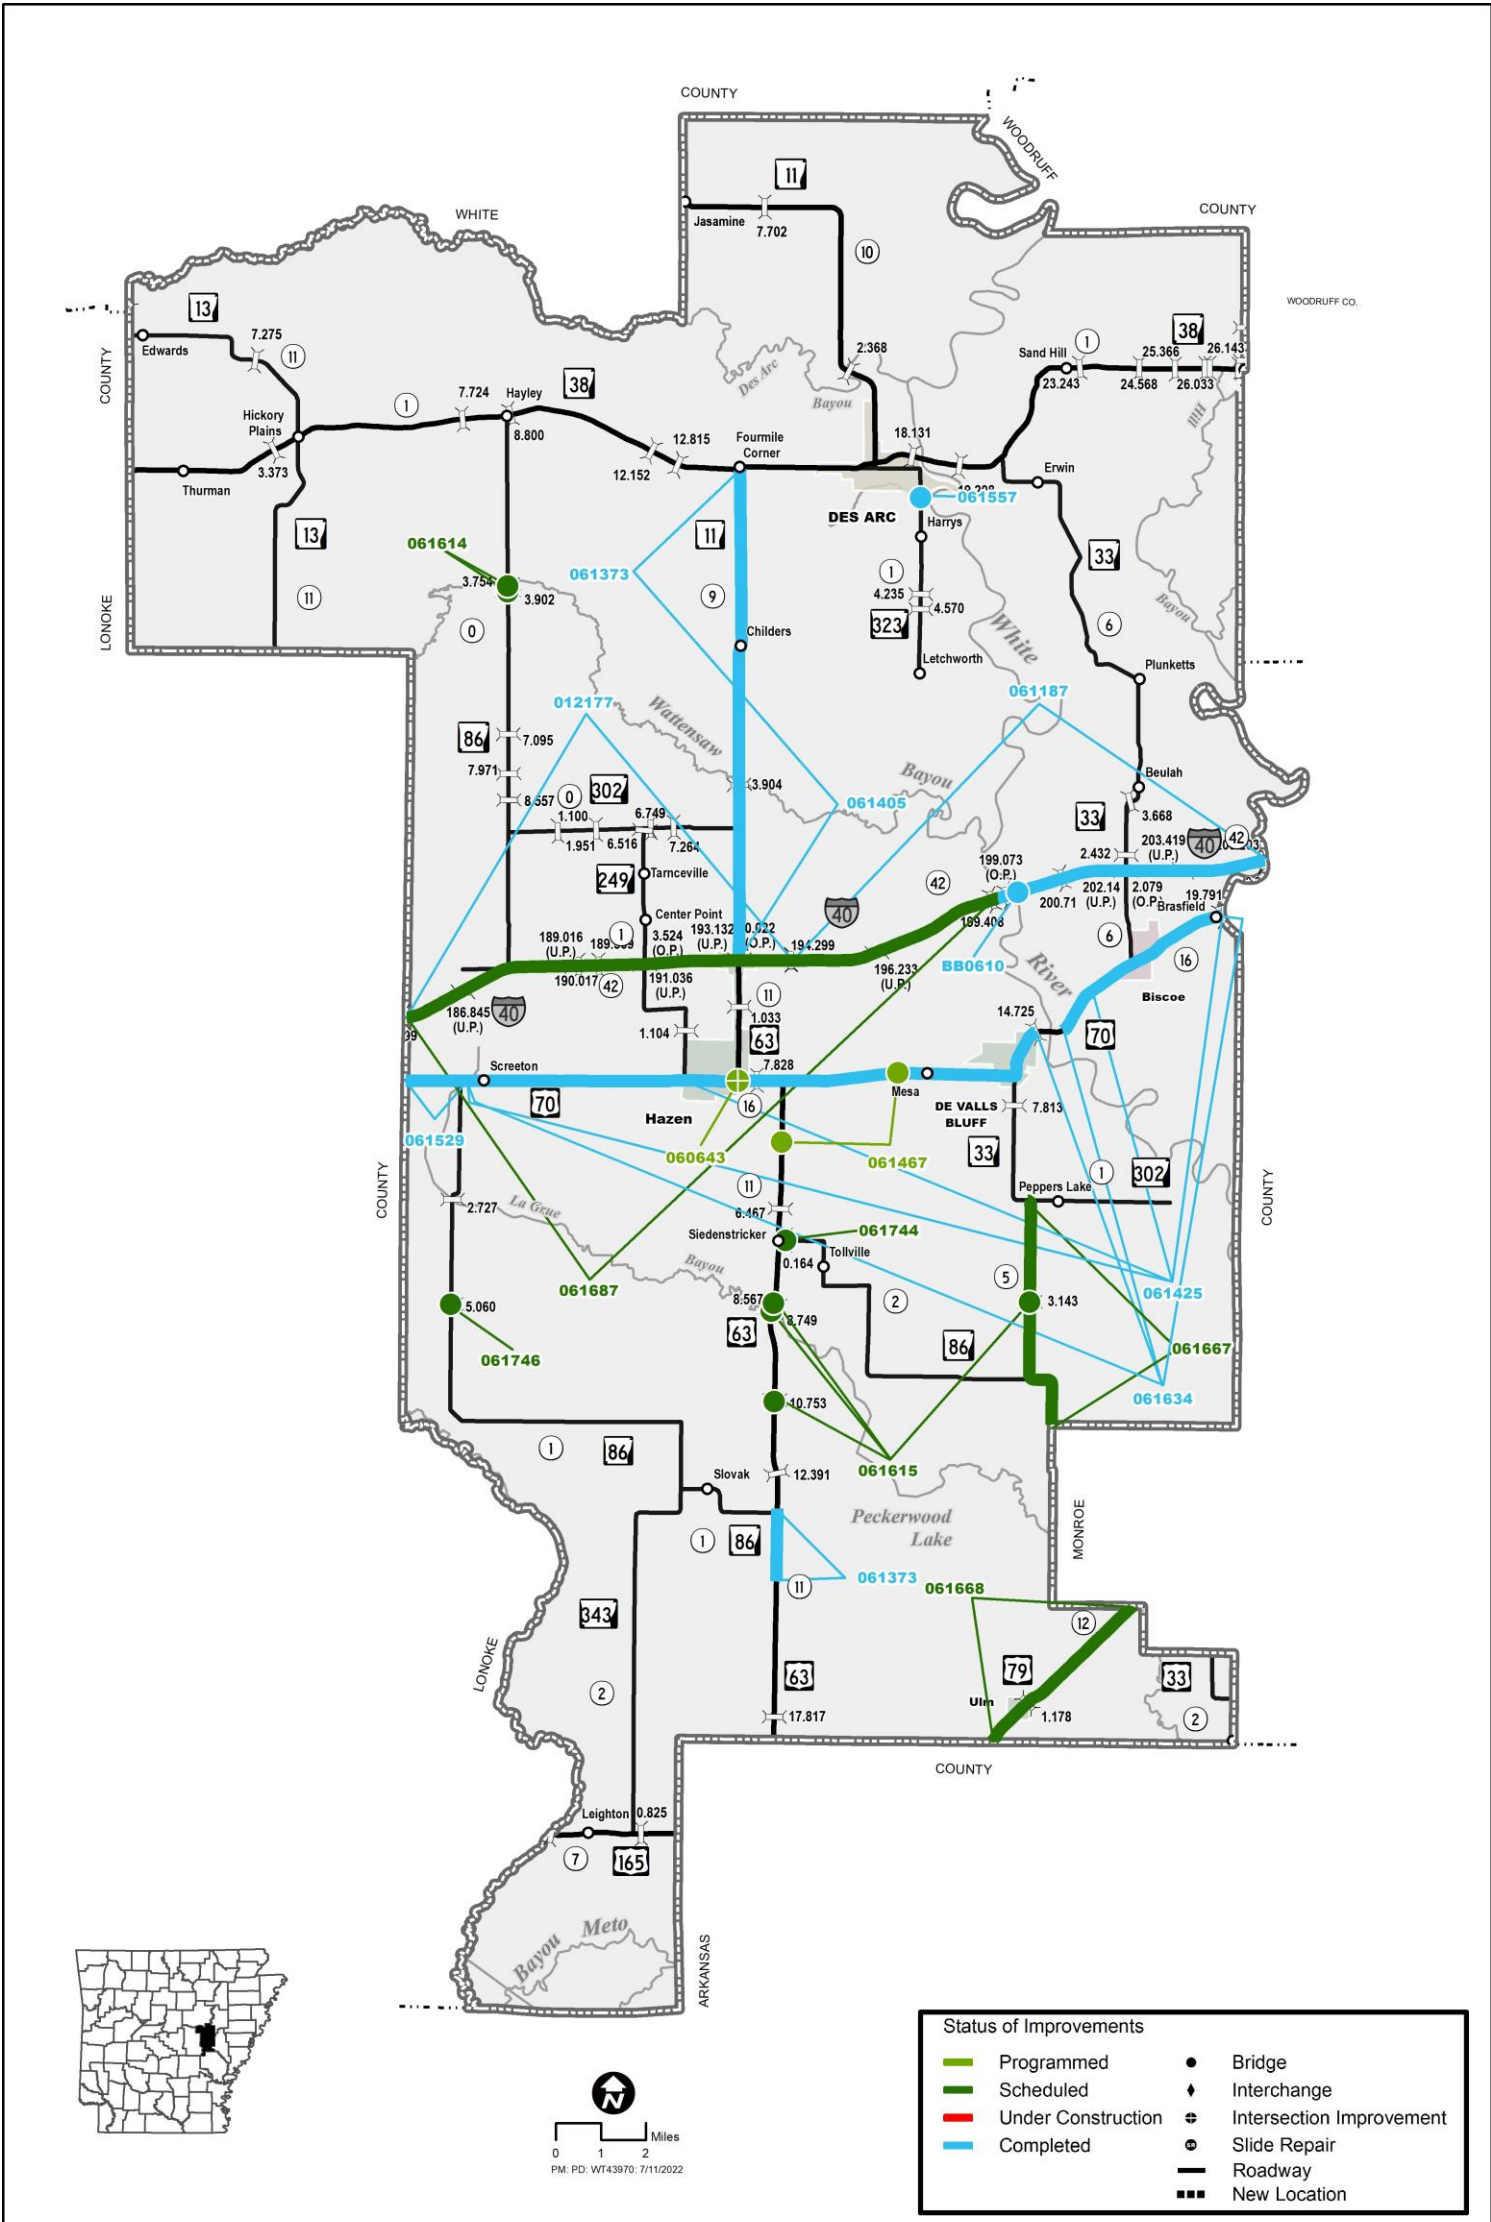

SUMMARY OF CONSTRUCTION PROJECTS

PRAIRIE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
012177	No. Little Rock – St. Francis Co. Ln. (Sel. Secs.) (Cable Median Barrier) (S) Addt'l Rte.-Sec.: Lonoke 40-41; Monroe 40-43; Pulaski 40-33	40	42	Safety Improvements	Completed	Feb. 2013	Sep. 2013	13.25	\$1,944,502	41.58	\$6,076,570
012387*	Statewide Underwater Br. Inspection (Phase XIII) (S) Addt'l Rte.-Sec.: Various	40	42	Miscellaneous	Programmed			-	-	-	-
012406*	Districts 1, 5, 6 & 10 Bridge Preservation (2022) (S) Addt'l Rte.-Sec.: Various	70	16	Bridge Rehabilitation	Under Construction	May. 2022	Mid 2023	-	\$1,080,210	-	\$7,187,312
012410*	Central AR – West Memphis ITS Impvts. Ph. 1 (S) Addt'l Rte.-Sec.: Various	40	42	Miscellaneous	Scheduled	Jun. 2023		-	< \$1 M	-	\$5 - \$10 M
012425*	Districts 2 & 6 Centerline Rumble Stripe Impvts. (S)			Safety Improvements	Under Construction	Apr. 2022	Early 2023	50.24	\$333,485	443.88	\$2,946,406
012440*	Central AR – West Memphis ITS Impvts. Ph. 2 (S) Addt'l Rte.-Sec.: Various	70	16	Miscellaneous	Programmed			-	< \$1 M	-	\$5 - \$10 M
060643	Hwy. 70/Hwy. 63N Intersec. Impvts. (Hazen)	63	11	Safety Improvements	Programmed			-	< \$1 M	-	< \$1 M
060828*	I-40 Landscaping (White River Rest Area) (S)	40	42	Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061187	Cache River – West (F)	40	42	Rehabilitation	Completed	Sep. 2011	Jul. 2013	10.35	\$56,324,788	10.35	\$56,324,788
061321*	DeValls Bluff RR Trail (ATEP-11) (S)			Enhancement	Completed	Jul. 2014	Nov. 2018	-	\$191,419	-	\$191,419
061373	Hwys. 11 & 63 (Sel. Secs.) (Overlay) (S) Addt'l Rte.-Sec.: Prairie 63-11	11	9	Resurfacing	Completed	May. 2012	Aug. 2012	6.63	\$1,320,090	6.63	\$1,320,090
061388*	White River Brs. Scour Repair (I-40 & Hwy. 38) (Prairie Co.) (S) Addt'l Rte.-Sec.: Prairie 38-1	40	42	Bridge Rehabilitation	Completed	Jul. 2013	Oct. 2013	-	\$1,265,112	-	\$1,265,112
061405	I-40 – North (Overlay) (S)	11	9	Resurfacing	Completed	Jun. 2013	Sep. 2013	5.96	\$886,982	5.96	\$886,982
061425	Hwy. 70 (Sel. Secs.) (Overlay) (S)	70	16	Resurfacing	Completed	Feb. 2014	Jul. 2014	8.49	\$1,550,308	8.49	\$1,550,308
061451*	Arkansas Tourist Information Center (White River) (S)	40	42	Roadside Appurtenances	Completed	Jan. 2016	Apr. 2017	-	\$4,826,680	-	\$4,826,680
061467	Hwy. 63 & Hwy. 70 Strs. & Apprs. (Prairie Co.) (S) Addt'l Rte.-Sec.: Prairie 70-16	63	11	Structure & Approaches	Programmed			0.95	\$5 - \$10 M	0.95	\$5 - \$10 M
061529	Hwy. 13 – Screeton (S) Addt'l Rte.-Sec.: Lonoke 70-15	70	16	Resurfacing	Completed	Jan. 2017	Nov. 2017	1.38	\$308,715	4.35	\$973,121
061557	Biene Creek Culvert Replacement (S)	323	1	Structure & Approaches	Completed	Jul. 2017	Oct. 2017	-	\$547,858	-	\$547,858
061614	Wattensaw Bayou & Relief Strs. & Apprs. (S)	86	0	Structure & Approaches	Scheduled	May. 2023		0.80	\$5 - \$10 M	0.80	\$5 - \$10 M
061615	La Grue Bayou, Wolf Island Slash & Honey Creek Strs. & Apprs. (S) Addt'l Rte.-Sec.: Prairie 63-11	33	5	Structure & Approaches	Scheduled	May. 2023		-	\$5 - \$10 M	-	\$5 - \$10 M

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

PRAIRIE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
061634	Pulaski Co. Line – Monroe Co. Line (Sel. Secs.) (S) Addt'l Rte.-Sec.: Lonoke 70-14/15	70	16	Resurfacing	Completed	Nov. 2020	Aug. 2021	17.82	\$4,306,247	37.65	\$9,098,216
061643*	District 6 Sealing Program (2020) (S) Addt'l Rte.-Sec.: Various	33	6	Sealing	Programmed			8.36	< \$1 M	69.72	\$1 - \$3 M
061647*	Des Arc Sidewalk Impvts. (TAP-21) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
061667	Monroe Co. Line – Hwy. 302 (S)	33	5	Resurfacing	Scheduled	2024		5.45	\$1 - \$3 M	5.45	\$1 - \$3 M
061668	Arkansas Co. Line – Monroe Co. Line (S)	79	12	Resurfacing	Scheduled	2024		4.38	\$1 - \$3 M	4.38	\$1 - \$3 M
061687	Hwy. 31 – East (S) Addt'l Rte.-Sec.: Lonoke 40-41	40	42	Resurfacing	Scheduled	Nov. 2022		13.73	\$15 - \$20 M	24.30	\$20 - \$30 M
061729*	Des Arc Trail Rehab. (RTP-20) (S)			Enhancement	Completed	Oct. 2021	Apr. 2022	0.43	\$62,500	0.43	\$62,500
061744	Oak Creek Str. & Apprs. (S)	86	2	Structure & Approaches	Scheduled	Jun. 2023		0.12	< \$1 M	0.12	< \$1 M
061746	South Branch La Grue Bayou Str. & Apprs. (S)	86	1	Structure & Approaches	Scheduled	May. 2023		0.03	< \$1 M	0.03	< \$1 M
A10017*	District 1 Resurfacing Program (2023) (S) Addt'l Rte.-Sec.: Various	33	2	Resurfacing	Programmed			2.46	< \$1 M	60.99	\$1 - \$3 M
A60018*	District 6 Resurfacing Program (2022) (S) Addt'l Rte.-Sec.: Hot Spring 171-5; Lonoke 31-2, 232-1; Prairie 302-0	38	1	Resurfacing	Programmed			5.98	< \$1 M	11.18	\$1 - \$3 M
A60020*	District 6 Resurfacing Program (2023) (S) Addt'l Rte.-Sec.: Various	33	5	Resurfacing	Programmed			12.58	< \$1 M	69.05	\$1 - \$3 M
BB0610	White River Str. & Apprs. (F)	40	42	Structure & Approaches	Sub. Completed	Nov. 2016	Jun. 2022	1.21	\$100,559,843	1.21	\$100,559,843
C59002*	Biscoe Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Sep. 2014	Nov. 2014	1.86	\$263,996	1.86	\$263,996
C59003*	Devalls Bluff Overlay (Sel.secs.) (S)	CS		Resurfacing	Completed	Sep. 2014	Oct. 2014	0.85	\$140,388	0.85	\$140,388
C59004*	Ulm Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Apr. 2015	Jun. 2015	2.00	\$157,645	2.00	\$157,645
C59005*	Hazen Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Jun. 2015	Nov. 2015	2.14	\$240,551	2.14	\$240,551
C59006*	Des Arc Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Feb. 2017	May. 2017	2.67	\$262,593	2.67	\$262,593
C59007*	Biscoe, Hazen, & Ulm Overlay (Sel. Secs) (S)	CS		Resurfacing	Completed	Jun. 2019	Oct. 2019	3.56	\$530,915	3.56	\$530,915
RX0022*	Hwy. 63 – East City Limits England (PE) Addt'l Rte.-Sec.: Arkansas 165-6; Lonoke 165-8	165	7	PE Only	Programmed			-	-	-	-
SA5941*	Prairie County Reseal No.3 (Sel. Secs.) (S)	CR		Sealing	Completed	Jul. 2012	Sep. 2012	3.20	\$83,230	3.20	\$83,230
SA5942*	Des Arc City Limits-West (Base) (S)	CR		Base	Completed	Sep. 2012	Nov. 2012	1.00	\$104,852	1.00	\$104,852
SA5943*	Prairie County Surfacing (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jul. 2013	Sep. 2013	5.80	\$249,738	5.80	\$249,738
SA5944*	Hwy. 302-Northwest (Base) (S)	CR		Base	Completed	Jul. 2013	Sep. 2013	1.90	\$215,818	1.90	\$215,818

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS
PRAIRIE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
SA5945*	Prairie Co Surfacing & Reseal(sel. Secs.) (S)	CR		Resurfacing	Completed	Jun. 2014	Aug. 2014	7.49	\$270,452	7.49	\$270,452
SA5946*	Prairie County Reseal No. 4 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jun. 2015	Sep. 2015	6.45	\$192,650	6.45	\$192,650
SA5947*	Prairie County Reseal No. 5 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jun. 2016	Sep. 2016	9.16	\$254,193	9.16	\$254,193
SA5948*	Prairie County Reseal No. 6 (Sel. Secs.) (S)	CR		Resurfacing	Completed	May. 2017	Aug. 2017	8.76	\$205,084	8.76	\$205,084
SA5949*	Prairie County Reseal No. 7 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jun. 2018	Aug. 2018	9.90	\$285,074	9.90	\$285,074
SA5950*	Co. Rd. 15 Reseal (S)	CR		Sealing	Completed	Jun. 2019	Sep. 2019	2.04	\$57,516	2.04	\$57,516
SA5951*	Hwy. 302 - North (Base) (S)	CR		Base	Completed	Jun. 2019	Sep. 2019	1.46	\$145,990	1.46	\$145,990
SA5952*	Prairie Co. Surfacing & Reseal (S)	CR		Resurfacing	Completed	Apr. 2021	Sep. 2021	7.64	\$315,681	7.64	\$315,681
SA5953*	Prairie County Reseal No. 8 (S)	CR		Resurfacing	Under Construction	May. 2022	Late 2022	8.44	\$325,185	8.44	\$325,185
Totals For All Projects In Prairie County								226.59	\$213,848,290		

* Job not shown on county map.
